

Airport East Precinct work: September 2019

The Australian and NSW Governments are upgrading roads east of Sydney Airport to improve traffic flow and access to the airport and Port Botany.

We are in our final stages of the project and work is progressing well. We have completed most of our work including:

- widened General Holmes Drive and Joyce Drive
- built the new rail bridge and installed new tracks
- built a shared path on Wentworth Avenue
- opened the Wentworth Avenue underpass
- installed new drainage and pumping station for storm water
- reconstructed the intersection of Joyce Drive and Qantas Drive



Work will continue on the final stages of paving, utilities, signal installation and landscaping. Standard construction hours for the **Airport East project** are from **7am to 6pm, Monday to Friday** and **8am to 1pm on Saturday**, excluding public holidays. Out of hours work will include up to **five-night shifts** from **9pm to 5am** during this week. Not all work during this time will be noisy.


September work includes:

- road works including milling, saw cutting, rock hammering and asphalt work on General Holmes Drive, Botany Road, Wentworth Avenue, Mill Pond Drive and Joyce Drive
- identifying utility locations and pavement investigation along Botany Road, Botany Lane, Bronti Street, Mill Pond Drive, Wentworth Avenue, Hardie Street, Beresford Street, General Holmes Drive and Joyce Drive
- construction work inside the site compound area on Wentworth Avenue and along the work areas on Botany Road and Wentworth Avenue including traffic light adjustment and sign installations
- footpath, kerb adjustment as well as concrete pouring of new kerb and medians along the project corridor
- installing traffic signal, kerb and concrete median along the project corridor
- delivery of construction vehicles and equipment to the work areas and use of the storage site in Dransfield Avenue.

Airport North Precinct work: September 2019

The NSW Government is upgrading roads north of Sydney's Kingsford Smith Airport to improve traffic flow and connections to and from the Airport and Port Botany.

Work on the project is progressing well. We are near to completing utility works underground in the coming months. We will also be completing asphalt work on O'Riordan Street near Robey and Baxter, this will allow us to complete our first traffic switch on to the newly laid road surface.

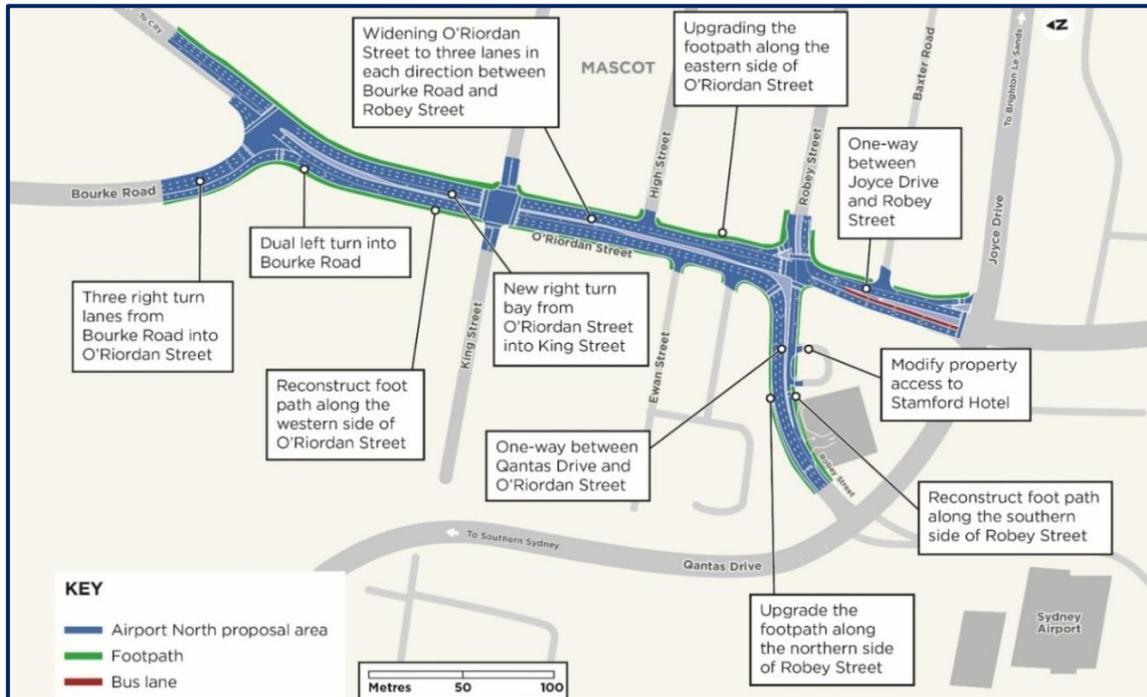

The work for September includes:

- road works including installing kerbs, footpaths and driveways as well as laying new asphalt
- identifying and relocating services on O'Riordan Street, Bourke Road, High Street, King Street, Robey Street and Baxter Road. This involves the use of a vacuum truck to safely excavate and trench underground services
- installing environmental controls including excavation and material removal along O'Riordan Street
- operating and monitoring groundwater dewatering systems 24/7
- use of site compounds at 166 and 200 O'Riordan Street for delivery and removal of equipment and materials
- traffic management and roadwork including footing installation and temporary traffic changes along O'Riordan Street between Bourke Road and Joyce Drive
- ongoing pedestrian changes and detours during construction work, please follow direction of signage. This includes the continued closure of the pedestrian footpath on the eastern side of O'Riordan Street between High Street and Baxter Road
- vegetation removal on O'Riordan Street.

Standard construction hours for the **Airport North project** are from **7am to 6pm, Monday to Friday and 8am to 1pm on Saturday**, excluding public holidays. Out of hours work for this week will include up to **five-night shifts**. Our night working hours are **9pm to 5am** and extended working hours on **Saturday** between **1pm and 6pm**.

There may be some noise, dust, vibration and disruption associated with this work. Machinery and equipment used may include trucks, excavators, paving machines, rollers, lighting towers, road saws, plate compactors, vacuum trucks, grinders, cranes, elevated work platforms, chainsaws, mulching machines, light vehicles, hand tools, concrete trucks and equipment. We will continue to make every effort to minimise the impacts to the local community.

If you have any questions about the work on either project, please contact our delivery partner, John Holland Group on **1300 862 844** or comms.airportprecinct@jhg.com.au.

For more information on our projects, visit www.rms.nsw.gov.au/sydneyairport.

Thank you for your patience during this important work.
